


Change Log 26th April 2021

Forecast -> Forecast Snapshot

- Added forecast variance by tracking actuals on data date and previous month forecast


Prev. Period Actuals	Prev. Period Forecast	Forecast Variance
\$2,797,052	\$16,574,7...	\$13,777,7...

These columns are hidden by default and can be accessed from column chooser

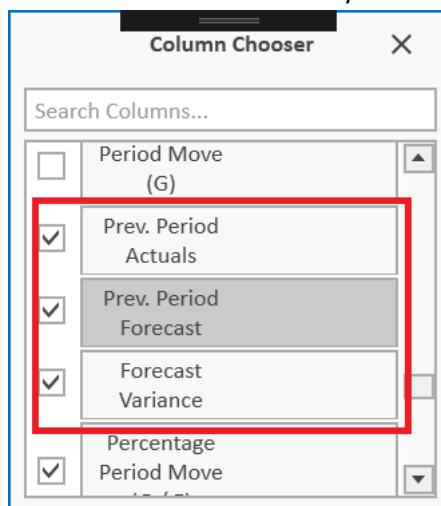


Clicking on the Prev. Actual cell will filter the details at the bottom

- Added ability to comment on forecast cells



Commented cells will show an information icon, mouse over the icon to see the comments



Change Log 24th March 2021

- Favourite Menu Items

- Project can be added to “My Projects” by clicking the uncolored star icon




- Project can be removed from “My Projects” by clicking on the colored star icon




- After clicking the star icon “Refresh Menu Items” will flash in green, indicating that there are projects that can be added or removed from “My Projects”. Clicking it will apply the changes.

Please note that this button is only visible when all windows are closed




Change Log 14th Dec 2021


- Forecast -> Forecast Snapshot
 - o Added forecast snapshot module that allows a snapshot of actuals, PO outstanding, PO Forecast, Indirect Forecast, Design earned and Budget to be saved for forecasting

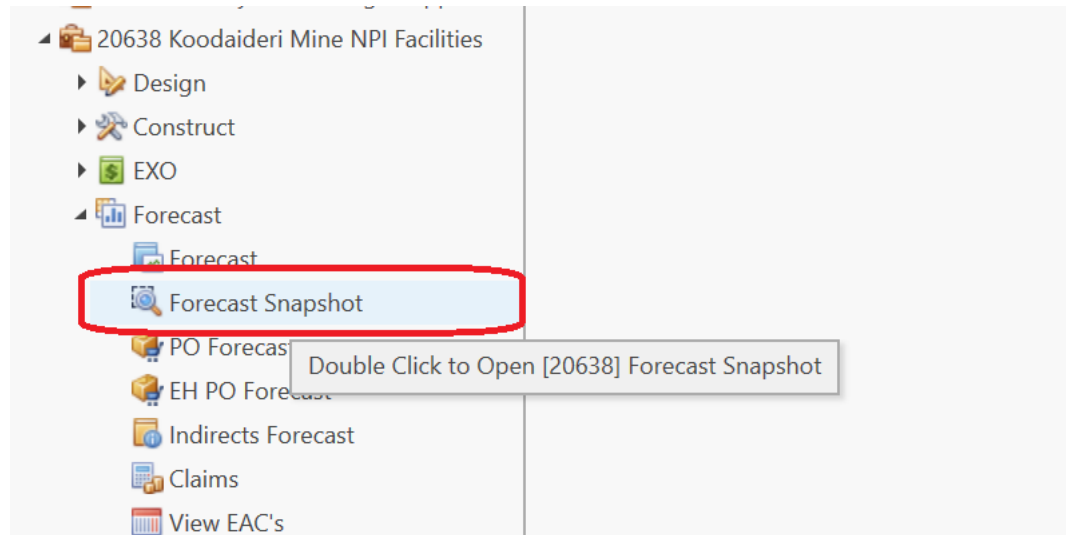

- o Snapshot can be refreshed by clicking 'Refresh Data'



- Forecast -> PO Forecast/EH PO Forecast/Indirect Forecast
 - o Added Save Snapshot button and prompt user to save snapshot when changes are detected

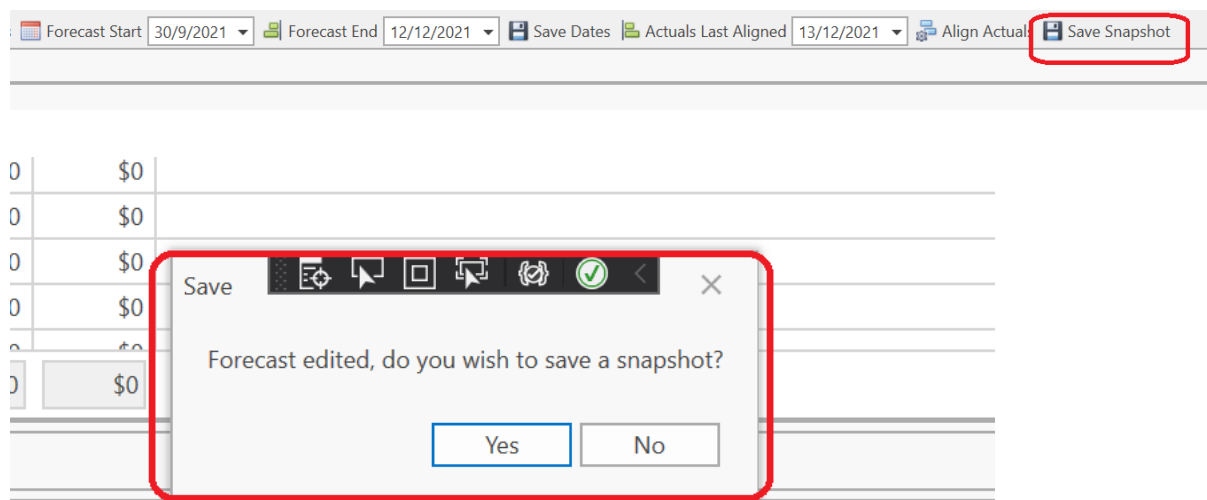

Change Log 9th Dec 2021

- Design -> Variation
 - o Newly added variation name must conform to VAR-### [Description] standard

[20638] Variations			
Drag a column header here to group by that column			
	Name	Type	Comments
✖	✖ VR-022	Design Change	
Variation name must be in this format, 'VAR-### [Description]'			
	VAR-001	Design Change	

- Construct -> Maintenance Cost/Charge Rates
 - o Added maintenance cost/charge rates maintenance

Projects

- ▲ Active
 - ▶ 00151 Lime Systems Design Support
 - ▲ 20638 Koodaideri Mine NPI Facilities
 - ▶ Design
 - ▲ Construct
 - Job Setup
 - ▶ Progress
 - Resource Allocation
 - Variations
 - Stages
 - ▲ Rates
 - Cost Rates [Direct]
 - Cost Rates [Chargeable Indirect]
 - Cost Rates [Maintenance]
 - Charge Rates [Direct]
 - Charge Rates [Add/Delete/Edit Maintenance Cost Rates and Enable Rates Scrapped from EXO]
 - Charge Rates [Maintenance]

Change Log 1st Dec 2021

- Design -> Progress
 - o Export/Import deliverables list by contractor

Copy Paste Cell Selection Save Layout Reset Layout Expand All Collapse All Export Import Show Earned % Against Budget Edit Report View Report Export Contractor List Import Contractor List Backward 28/11/2021 Forward

[00151] Design Progress

Drag a column header here to group by that column

Properties (Read Only)															Editable Properties	
Phase	Area	Sub Area	Discipline	Discipline Number	Document Type	Deliverable Type	Department	Internal Number	Client Number	Primary Title	Secondary Title	omment	Sub Job	Office	Contractor	Gate
Click here to add a new row																
D1	001		Structural	1	Calculation	Deliverable	Engineering	00151-CAL-ST-012		Horsco Bag Breaker Calculation			00151-001-00-D1		Contractor	TEST 1
D1	001		Structural	1	Calculation	Deliverable	Engineering	00151-CAL-ST-038		Horsco Bag Breaker Calculation			00151-001-00-D1		Contractor	TEST 1
D1	001		Structural	1	Calculation	Deliverable	Engineering	00151-CAL-ST-004		Horsco Bag Breaker Calculation			00151-001-00-D1		Contractor	TEST 1
D1	001		Structural	1	Calculation	Deliverable	Engineering	00151-CAL-ST-012		Horsco Bag Breaker Calculation			00151-001-00-D1		Contractor	TEST 1
D1	001		Structural	1	Calculation	Deliverable	Engineering	00151-CAL-ST-012		Horsco Bag Breaker Calculation			00151-001-00-D1		Contractor	TEST 1
D1	000		General Engineering	1	Management	Deliverable	Engineering Management	TESTTEST2		Design Management		TEST2	00151-000-00-D1		Contractor	
D1	000		General Engineering	1	Management	Deliverable	Engineering Management	TESTTEST3		Design Management		TEST2	00151-000-00-D1		Contractor	
D1	000		General Engineering	1	Management	Deliverable	Engineering Management	TESTTEST3		Design Management		TEST3	00151-000-00-D1		Contractor	
D1	000		General Engineering	1	Management	Deliverable	Engineering Management	TESTTEST5		Design Management		TEST3	00151-000-00-D1		Contractor	
D1	000		General Engineering	1	Management	Deliverable	Engineering Management	TESTTEST4		Design Management		TEST3	00151-000-00-D1		Contractor	

- Contractor
 - o Add/Edit/Delete contractor

Search [00151] Contractors

Drag a column header here to group by that column

Name
TEST 1

Dashboards

- My Dashboard
- My Deliverables
- My Design Timesheet
- Review Timesheets
- Document Control

Projects

- Active
 - 00151 Lime Systems Design Support
 - Design
 - Deliverables
 - Progress
 - Progress Distribution
 - Variations
 - Variations Breakdown
 - Deliverable Gates
 - Job Permissions
 - Rates
 - Construct
 - EXO
 - Forecast
 - Registers
 - Areas
 - Sub Jobs
 - Holidays
 - Packages
 - Contractors
 - HSE
 - Monthly HSE report

Add/Delete/Edit Project's Contractor

Change Log 12th Nov 2021


- Design -> Progress
 - o Added contractor progress update export/import
[Tutorial](#)

Change Log 18th Oct 2021

- Exo Resources
 - o Add/Edit no longer affect both locale (Perth/Montreal) and only updates depending on which version of BluePrints is installed (Perth/Montreal)

Change Log 29th Sep 2021

- Timesheet Entry
 - o Restricted to only querying a single week. With start date automatically adjusted to Monday to avoid duplicate records

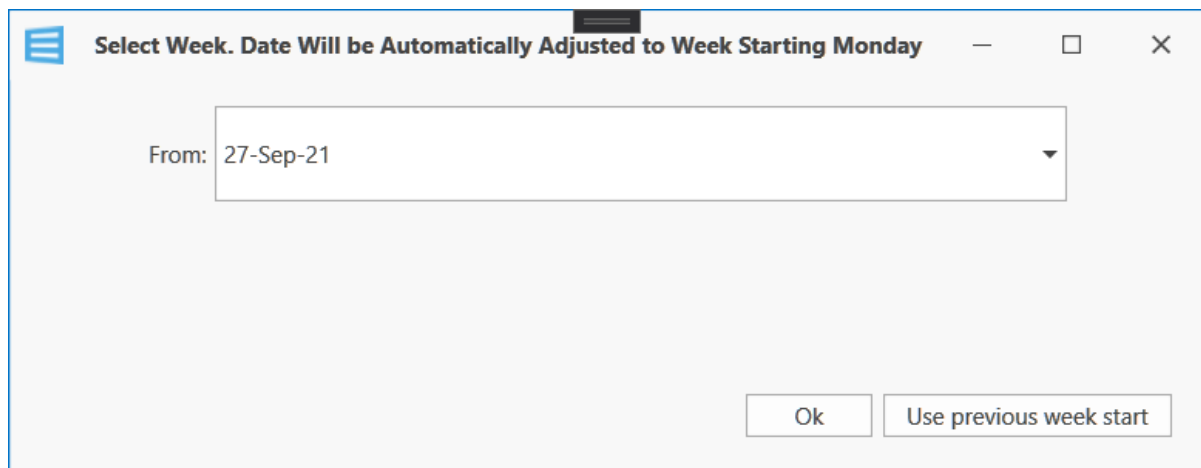

Select Week. Date Will be Automatically Adjusted to Week Starting Monday

From: 27-Sep-21

Ok Use previous week start

Change Log 17th Sep 2021

Design -> Job Permission, Construction -> Resource Allocation, EXO -> Master Job Permission

- Added bulk assign/unassign users

The screenshot shows the software interface with the 'Job Permissions' section highlighted in the left sidebar. The main panel displays a list of users with checkboxes for 'Can Book' and 'User'. A red box highlights the 'Bulk Assign Users' button.

Design -> Job Permission


- Show all users even when they are not linked to EXO
- Show error message when user tries to add a resource that is not linked to EXO

The screenshot shows a table with columns 'Can Book' and 'User'. The 'Can Book' column has a red 'X' icon. The 'User' column shows 'Vijay Bhavsar'. A red box highlights the 'Can Book' column header. Below the table, a message box states: "User isn't linked to EXO, please link user to EXO in Data -> Users column Perth EXO and Montreal EXO".

Change Log 15th Sep 2021

- S-Curve and Progress

- Added ability to set % benchmark measures against budget/current units




- Generated report will also reflect the same measure


Change Log 1st Sep 2021

- Rates

- Rates for design has been moved into design category
- Old

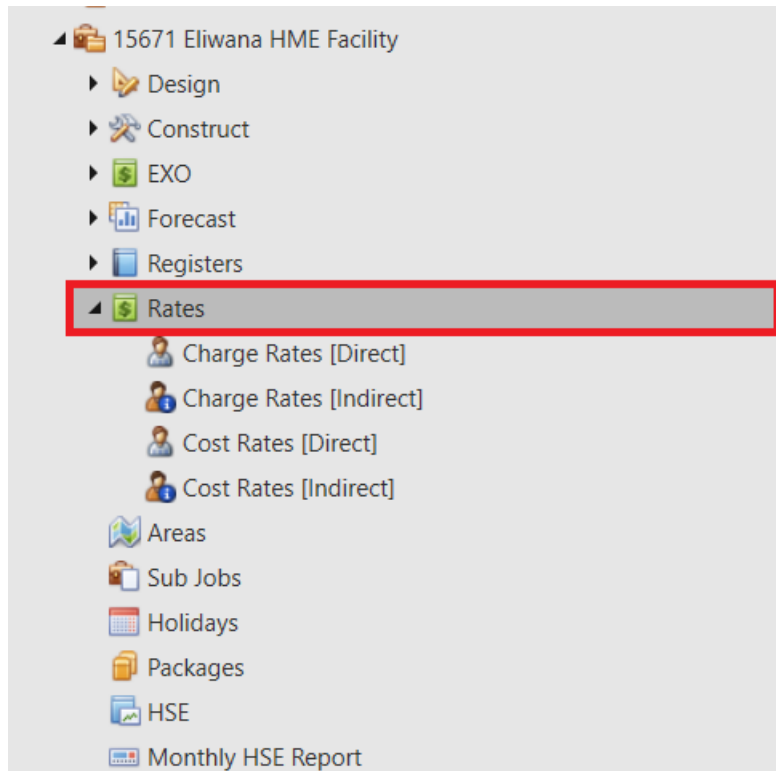

○ New

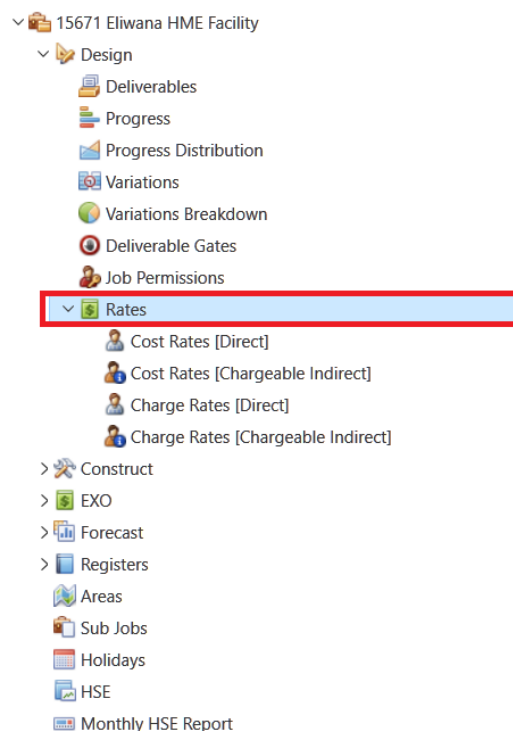

- Improved S-Curve/Forecast loading

- Added Equipment Hire PO forecast which allows forecasting by stock code

Search

[15671] Forecast [20638] EH PO Forecast

Drag a column header here to group by that column

PO Number	Variation	Stock Code	Description	Narrative	Supplier	Invoiced Prior Month	First Raised	PO Hdr Last Updated
100140		EH-MP-004	HIRE Excavator 30T		Perth Construction Hire...	\$0.00	01/05/2021	31/08/2021
100486	VR-124 Te...	EH-FP-003	1 X 500kVA Generator		UON Pty Ltd	\$0.00	10/06/2021	30/08/2021
100530		EH-SI-006	Permit Room 12.0m x 3.0m	Building being moved by Primo... Please note this building has been... Hire duration is estimate only and...	AUSCO MODULAR PTY L...	\$0.00	11/06/2021	30/08/2021
100624		EH-FP-022	DLR010HD DUCTOR TESTER HIRE	INDICITIVE TIME FRAME PER DAY	Techcorp Services (Platin...	\$0.00	15/06/2021	13/08/2021
100626		EH-FP-022	Megger DLRO10X Microhmmer	QS29943	TR Hire Pty Ltd	\$0.00	15/06/2021	18/08/2021
102225		EH-FP-022	ductor tester hire per day	new Po to cover hire extension of...	Techcorp Services (Platin...	\$0.00	06/07/2021	21/07/2021
102674	VR-222 (S...	EH-SI-009	10,000Lt Fuel Tank - Day Rate Hire	Hire duration is estimate only and...	UON Pty Ltd	\$0.00	20/07/2021	30/08/2021
102674		EH-FP-003	Freight for G416-500 & FT129	direct back charge to Worley unde...	UON Pty Ltd	\$0.00	20/07/2021	30/08/2021
102674	VR-222 (S...	EH-FP-003	500kVA Generator - Day Rate Hire		UON Pty Ltd	\$0.00	20/07/2021	30/08/2021
103998	VR-235 (S...	EH-HV-004	Vermeer Vsk 1200 Day Rate	Required for 12 hours (\$345 per h... RFQ - Non Destructive excavation... Hire duration is an estimate only a... Hire commencement date TBA - Li...	FRC Hire Pty Ltd	\$0.00	30/08/2021	30/08/2021
81624		EH-SI-003	5 x Waste Tank 6000L - Day Rate		AUSCO MODULAR PTY L...	\$0.00	12/02/2020	30/08/2021
81624		EH-SI-001	1 x Central Facilities: Office Complex		AUSCO MODULAR PTY L...	\$0.00	12/02/2020	30/08/2021
81624		EH-SI-002	2 x Toilet 6.0m x 3.0m All Male		AUSCO MODULAR PTY L...	\$0.00	12/02/2020	30/08/2021
81624		EH-SI-006	1 x 12x6 Lunchroom Complex - Da...		AUSCO MODULAR PTY L...	\$0.00	12/02/2020	30/08/2021
83188		EH-MP-013	Knuckle Boom - Z45ft (13.7m) - D...	12 Month Hire Hire Duration iis estimate only and... Machine is to be in near new cond... Weekly rate is \$650p/week	Access Hire Australia	\$0.00	11/03/2020	26/08/2021
83360		EH-TL-002	10' Dangerous Goods		Royal Wolf Trading Austr...	\$0.00	18/03/2020	27/07/2021
83520		EH-LV-003	21 Seat Bus Hire		Fleetspec Hire	\$0.00	26/03/2020	27/07/2021
83944		EH-LV-004	50 seater bus hire		Fleetspec Hire	\$0.00	20/04/2020	02/08/2021
84285		EH-LV-004	58 seater bus hire (2nd bus)		Fleetspec Hire	\$0.00	04/05/2020	25/08/2021
84514		EH-MV-001	Compact Track Loader - Day Rate	CAT 259D - Start Date 15/4/2020	ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-FP-008	Off hire charges - plate compactor		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-MP-003	15KL 6x4 Watercart - Hourly Rate		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-MP-007	3T-Tele-Handler - Day Rate		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-MP-001	Compact Track Loader - Day Rate		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-MP-002	Excavator (8.5T) w/ 3 Buckets - Da...		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-HV-003	enviro Levy		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021
84514		EH-HV-002	15KL 6x4 Watercart - Hourly Rate		ESM Resources Pty Ltd	\$0.00	12/05/2020	01/09/2021

02905 Lynas Design Support
 02907 Mt Weld Water Treatment Plant - Cost Study
 02910 Mt Weld RWTP - FEED
 03414 WTS2 Supply Electrical Labour
 03608 South Flank Fuel Facilities
 06728 Mt Magnet Scraper Station Metering
 07238 Macedon Low Pressure Compressor Operation
 07241 Fuel Facility Load Commissioning
 07244 South Flank Refuelling Flow Rate Reduction
 08708 Torrens Island Power Station
 10008 Cloudbreak PCP ROM Wall and Structural Design
 10009 HOPPER 9 CONSTRUCTION
 10012 Solomon Queens Crushing Plant D&C
 10013 FMG Queens Overland Conveyor Supply & Construct
 10018 West Project Hub PCP
 13012 Mt Webber Arc Flash Assessment
 14102 Black Swan Restart
 15671 Eliwana HME Facility
 15678 CC WHIMS Plant Improvements
 15685 Tasmania Green Hydrogen Project
 16902 Site Engineering Support
 16916 Nova Nickel Misc Site Works
 16919 M&A Tasks
 17511 Sino Stockyard Services Relocation
 17516 DECONTAMINATION UNIT INSTALLATION
 17599 Sino MSA Projects
 17805 BHP Finucane Island Port Lab
 18605 Piedmont DFS
 20006 Geraldton Crude Export Facility
 20503 Laboratory Electrical Installation
 20619 Lake Macleod Radial Stacker Replacement (DSL)
 20638 Koodaideri Mine NPI Facilities
 Design
 Construct
 FXO
 Forecast
 Forecast
 PO Forecast
 EH PO Forecast
 Indirects Forecast
 Claims
 View EAC's

Change Log 8th July 2021

- Design -> Progress
 - Start date is changed to show planned P6 start date instead of summarized to w/e
 - Due date is changed to show planned P6 end date instead of summarized to w/e
 - Forecast Finish date is changed to show remaining P6 end date instead of summarized to w/e

[00021] Design Progress																											
Drag a column header here to group by that column																											
Editable Properties				Budget (Read Only)				Cumulative To Date (Read Only)								Cumulative Total (Read Only)				Period (Read Only)				Product			
Job	Gate	Current %	Target Start	Target End	Budget Hours	Adjusted Budget	Variation Hours	Approved Variations	Total Hrs	Remaining Hrs	User Remaining Hrs	Total Change	Baseline %	Schedule %	Start Date	Due Date	Forecast Finish Date	Next Release Date	Total Earned Units	First Earned Date	Last Earned Date	Total %	Total Burned Units	Planned %	Earned %	Earned Units	Current Product
Click here to add a new row																											
M21-001-00-01	DD1...	0%	2%		100.00	100 hrs	0.00	Expand...	100.00	100.00	0.00	\$13,200.00	0.00%	0.00%		21/12/2021	07/12/2021		0.00			0%	0.00	0.00%	0.00%	0.00	

Change Log 16th June 2021

- Design -> Variation
 - o Added button to add variation code to EXO without submitting variation

The screenshot displays the Siemens Teamcenter user interface. At the top, a toolbar contains various icons for file operations like 'Refresh', 'Delete', 'Copy', 'Paste', 'Save Layout', 'Export', 'Import', 'Summarize Variations', 'Edit', 'Submit', 'Approve', 'Client Approve', 'Update XSD body', and 'Add Variation Code to Item'. The 'Add Variation Code to Item' icon is highlighted with a red box.

The main workspace is divided into two panes. The left pane shows a hierarchical tree structure with categories like 'Dashboards', 'Projects', 'Deliverables', and 'Variations'. The 'Variations' category is selected and expanded, showing sub-items like 'Progress', 'Variations Breakdown', 'Deliverables', 'Job Permissions', 'Construct', 'ECO', 'Forecast', 'Registers', 'Rules', 'Events', 'Sub Jobs', 'Holidays', and 'Risk'. The 'Variations Breakdown' item is highlighted.

The right pane displays a table titled '00101 Variations'. The table has columns for 'Name', 'Type', and 'Comments'. Below the table, there is a button 'Click here to add a new row'. To the right of the table, there is a vertical toolbar with icons for 'Copy With Headers', 'Copy', 'Paste', 'Bulk Edit', 'Set Up', 'Fit Down', 'Edit', 'Submit', 'Approve', 'Client Approve', 'My Variation Code', and 'Add Variation Code to Item'. The 'Add Variation Code to Item' icon is highlighted with a red box.

Change Log 2nd June 2021

- Exo Resources
 - o Allow addition of BP user from EXO Resources by checking “Is BP User” checkbox

Search

Drag a column header here to group by that column

Name	Title	Security Profile	User Profile	Discipline Code	Commodity Code	Sales GL	Purchase GL	Cost GL	Payroll Id	Report To	Default Stock Code	Short Code	Is BP User
RYAN MCFARLANE	CHIEF FINANCIAL OFFICER	Salary	Timesheet Manager	OVERHEAD	002 Administrat...	Reven...	Subcontra...	Sub...			RMD	RMD	☒
ALAN PAGE	MECHANICAL DESIGNER	OT45	STAFF	DRAFTING	002 Lead Mech...	Reven...	Subcontra...	Sub...			APD	APD	☒
GRANT THOMAS	LEAD STRUCTURAL DESIGNER	OT45	STAFF	DRAFTING	003 Lead Struct...	Reven...	Materials	Sub...			GT1	GT1	☒
PETER GROSSBY (CAN)	PRINCIPAL STRUCTURAL ENGINEER	Canada	Timesheet Manager	ENGINEERING	001 ENGINEERL...	Reven...	Subcontra...	Sub...			PG2	PG2	☒
BEN DAVIES	PRINCIPAL MECHANICAL ENGINEER	Salary	Timesheet Manager	ENGINEERING	002 Principal M...	Reven...	Subcontra...	Sub...			KD0	KD0	☒
CAMERON KENNY	PROJECT MANAGER	Salary	OVERHEAD	006 Business D...	Reven...	Materials	Sub...	Sub...			CHD	CHD	☒
DEAN BRICOGVIC	SITE MANAGER/PROCESS PLANT...	Salary	Timesheet Manager	PROJECT MA...	001 Project Ma...	Reven...	Subcontra...	Sub...			DE0	DE0	☒
NICHOLAS DUNNE	CARPENTER TRADESMAN	FlatRate	STAFF	TRADES & LA...	008 Carpenter T...	Reven...	Subcontra...	Sub...			ND0	ND0	☐
BRADLEY PALMER	CIVIL SUPERVISOR	FlatRate	STAFF	TRADES & LA...	008 Carpenter T...	Reven...	Materials	Sub...			BP1	BP1	☐
KELLY DAWSON	HUMAN RESOURCES COORDINAT...	PT40	Timesheet Manager	OVERHEAD	002 Administrat...	Reven...	Materials	Sub...			KD0	KD0	☒
NATASHA BRANCO	ELECTRICAL ENGINEER	Salary	STAFF	DRAFTING	012 PIPING DES...	Reven...	Subcontra...	Sub...			NB0	NB0	☒
KAU SIKSINI	CRANE OPERATOR	PenaltyRate-LB	STAFF	OPERATIONS...	001 Project Ma...	Reven...	Materials	Sub...			TCC-45-P-04-D	K51	☐
NICHOLAS WEDDON	CONTRACTS MANAGER	Casual	STAFF	CONSTRUCT...	005 Mechanical...	Reven...	Subcontra...	Sub...			NW0	NW0	☐
NICK BONNER (RUS)	CONTRACTS MANAGER	Contractor	STAFF	PROJECT MA...	001 Project Ma...	Reven...	Materials	Sub...			9000026	NB1	☒
SU BING-WEN	SCHEDULER	Salary	STAFF	PROJECT MA...	006 SCHEDULER	Reven...	Subcontra...	Sub...			S80	S80	☒
MICHAEL DUNNIS	SENIOR STRUCTURAL ENGINEER	OT45	Timesheet Manager	ENGINEERING	003 Structural E...	Reven...	Subcontra...	Sub...			M40	M40	☒
RYAN BARNES	MECHANICAL DESIGNER	Salary	STAFF	DRAFTING	004 Mechanical...	Reven...	Materials	Sub...			R81	R81	☒
MAURO MALTEZ (DUAL CAD)	DRAWING OFFICE MANAGER	Contractor	STAFF	DRAFTING	005 Structural D...	Reven...	Materials	Sub...			981887	MM9	☒
BEN GROSSBY	DRAWING OFFICE MANAGER	OT45	Timesheet Manager	DRAFTING	001 Drawing Off...	Reven...	Subcontra...	Sub...			850	850	☒
DANIEL SCUDDER	LEAD PIPING DESIGNER	OT45	STAFF	DRAFTING	009 LEAD PIPIN...	Reven...	Materials	Sub...			D50	D50	☒
LIAM SHONCHON	ESTIMATOR	Salary	STAFF	OVERHEAD	001 Estimatio...	Reven...	Subcontra...	Sub...			L50	L50	☒
GAVIN SATTE	PROJECT MANAGER	Salary	STAFF	SM01 - SITE...	001 Project Ma...	Reven...	Revenue	Sub...			2088	G50	☒
NATHAN MATTHEWS (CEM ALLIAN...	CONSTRUCTION MANAGER	Contractor	STAFF	CONSTRUCT...	012 COMMISSI...	Reven...	Materials	Sub...			9990025	NM1	☒
JOHN GIANONCELLI (PERTH REC)	CONSTRUCTION MANAGER	Contractor	STAFF	CONSTRUCT...	001 Constructio...	Reven...	Subcontra...	Sub...			999611	J50	☒
KETH SUBRTSKY	MECHANICAL FITTER	PenaltyRate-LB	STAFF	TRADES & LA...	003 Mechanical...	Reven...	Materials	Sub...			TMF-02-P-02-D	K50	☒
DEREK MCCUNE	ELECTRICAL SUPERVISOR	FlatRate	STAFF	CONSTRUCT...	007 Electrical E...	Reven...	Subcontra...	Sub...			185	DM0	☒
FRANK MORELLINI	HSE ADVISOR	Salary	Timesheet Manager	CONSTRUCT...	002 HSE Advisor	Reven...	Materials	Sub...			1937	FM0	☒
THOMMY RATTIGAN	LEAD ELECTRICAL DESIGNER	OT45	Timesheet Manager	DRAFTING	007 Electrical D...	Reven...	Materials	Sub...			238	TR0	☒
SAMMY TREWHITT	PROCESS ENGINEER	Salary	STAFF	ENGINEERING	009 PROCESS E...	Reven...	Materials	Sub...			297	ST1	☒
RYAN MCFARLANE	ACCOUNTS/PAYROLL	Casual	Timesheet Manager	OVERHEAD	002 Administrat...	Reven...	Subcontra...	Sub...			384	384	☒
AUSTIN SPORRE	PROJECT MANAGER	Salary	Timesheet Manager	OVERHEAD	001 Estimatio...	Reven...	Subcontra...	Sub...			1069	J55	☒
AARON HUGGETT	PROJECT MANAGER	Salary	Req And Time Manager	PROJECT MA...	003 Electrical P...	Reven...	Subcontra...	Sub...			133	AH0	☒
CHRIS WADE (WADE CONTRACT...	PROJECT MANAGER	Contractor	Timesheet Manager	PROJECT MA...	001 Project Ma...	Reven...	Subcontra...	Sub...			9000033	CW0	☒
KAYNE FERRIS (DOO)	GRADUATE ENGINEER	Contractor	STAFF	ENGINEERING	007 Graduate E...	Reven...	Subcontra...	Sub...			9004567	KF1	☒
NED HAMBURG	DESIGN MANAGER	Salary	Timesheet Manager	ENGINEERING	002 Principal M...	Reven...	Subcontra...	Sub...			114	NH0	☒
GLEN BRICOGVIC	SENIOR PROCUREMENT OFFICER	Salary	Req And Time Manager	PROJECT MA...	004 Procureme...	Reven...	Subcontra...	Sub...			78	G51	☒
PETER McDONALD	CONSTRUCTION/PROJECT MANA...	Casual	STAFF	CONSTRUCT...	001 Constructio...	Reven...	Subcontra...	Sub...			180	PM2	☒
DANIEL O'CONNELL	CIVIL SUPERVISOR	FlatRate	STAFF	CONSTRUCT...	010 CIVIL SUPE...	Reven...	Materials	Sub...			209	DO0	☒
KIM STOTT	PROJECT MANAGER	Salary	Req And Time Manager	PROJECT MA...	001 Project Ma...	Reven...	Materials	Sub...			1994	K53	☒
MATTHEW ADAMS	FORMWORK CARPENTER	PenaltyRate-LB	STAFF	TRADES & LA...	008 Carpenter T...	Reven...	Materials	Sub...			1933	MA0	☒
ANDREW MCCORMIE	METAL TRADEPERSON	Casual	STAFF	TRADES & LA...	001 BMM/Pipin...	Reven...	Materials	Sub...			1862	TL-093CA	☒
CHAZZO GABY	ELECTRICIAN	FlatRate	STAFF	CONSTRUCT...	013 ELECTRICA...	Reven...	Materials	Sub...			95	C01	☒
CLINTON RICHARDSON	PROCUREMENT EXPEDITOR	Salary	HsqPQHntUser	PROJECT MA...	004 Procureme...	Reven...	Subcontra...	Sub...			242	CR0	☒
VALESIA TAPLEY	ACCOUNTS MANAGER	Salary	Req And Time Manager	OVERHEAD	002 Administrat...	Reven...	Materials	Sub...			287	VMD	☒
TIM WALTHAM	PROCUREMENT EXPEDITOR	Salary	Regulation Manager	PROJECT MA...	004 Procureme...	Reven...	Materials	Sub...			311	TW0	☒
RICHARD WOODMAN	MECHANICAL PROJECT ENGINEER	Salary	STAFF	PROJECT MA...	002 MECHANIC...	Reven...	Subcontra...	Sub...			225	RMD	☒
BRETT GROSVENOR	SITE MANAGER/PROCESS PLANT...	Salary	Timesheet Manager	PROJECT MA...	001 Project Ma...	Reven...	Subcontra...	Sub...			109	BG2	☒
SHANE IMORUND	HSE ADVISOR	Salary	STAFF	CONSTRUCT...	002 HSE Advisor	Reven...	Materials	Sub...			1375	S11	☒
ANTHONY VAN DOORNUM	PIPING DESIGNER	Casual	STAFF	DRAFTING	012 PIPING DES...	Reven...	Subcontra...	Sub...			515	TV0	☒
DARREN McDONALD	MECHANICAL PROJECT ENGINEER	Salary	Req And Time Manager	PROJECT MA...	002 MECHANIC...	Reven...	Subcontra...	Sub...			181	DM2	☒
IAN MONTGOMERY	PERSON MANAGER	Casual	STAFF	DRAFTING	001 Person Ma...	Reven...	Materials	Sub...			1708	DR-0118	☒

Users

Drag a column header here to group by that column

Sub Job

Department

Commodity Code Desc

Resource

Title

Translate

Quantity

Unit Rate

Cost

Status

- Exo -> Transactions
 - o Allow slower load times but faster edit/sort/filter operation by clicking “Download Data”, preference is saved for all projects

Search

Drag a column header here to group by that column

Sub Job	Department	Commodity Code Desc	Resource	Title	Translate	Quantity	Unit Rate	Cost	Status

Download Data

Change Log 20th May 2021

- Added option to trim inactive users by referencing EXO (according to user's office). Trimmed users will have “Leave Date” set as today

Refresh Delete Row Undo Redo Copy Paste Cell Selection Save Layout Reset Layout Expand All Collapse All Export Import Update User(s) Update EXO Name Trim Inactive Users Hide User Impersonate

Users

Drag a column header here to group by that column

Login Name	First Name	Last Name	Department	Discipline	Title	Description	Role	Authorised Projects	Office	Perth EXO	Montreal EXO	Approver	Utilisation	Start Date	Leave Date	Professional Membership	Membership Number
Aaron.huggett	Aaron	Huggett	Project M...	Offsite...	Electri...	Electrical...	Engin...	0000015001...	Perth	AARON...	AARON HU...	Dean.E...		13/06/20...	20/05/20...		
Abdel.El...	Abdel	Elbakir	Engineer...	Electrical	Lead...	Lead EIC...	Engin...	All	Mont...			Peter.G...		08/03/20...			
Ada.Ceras...	Ada	Cerasuolo	Administr...	Office...	Office Ad...	Office Ad...	Admi...	All	Mont...	ADA CE...	ADA CERAS...	Jacque...		13/12/20...	20/05/20...		
Adam.Gryl...	Adam	Gryl	Engineer...	Mechan...	Princi...	Princi...	Disci...	All	Perth	ADAM...	ADAM GRYL	Ben.Da...		29/05/20...	20/05/20...		
Adela.Cris...	Adela	Cristea	Drafting	Mechan...	Senior M...	Senior M...	Lead...	All	Mont...	ADELA...	ADELA CRIS...	Frederi...		24/09/20...	20/05/20...		
adrian.orl...	Adrian	Orlando	Engineer...	Senior...	Senior P...	Senior P...	Engin...	All	Perth	ADRIA...		Ben.Da...		14/10/20...	20/05/20...		
Akhil.Shukla	Akhil	Shukla	Project M...	General...	Senior Pl...	Senior Pl...	Cost...	10012:10013:15660	Perth	AKHIL S...		Rory.Fr...		17/01/20...	20/05/20...		
alan.bolton	Alan	Bolton	Site Mana...	Site H...	Site Healt...	Site Healt...	Admi...	All	Mont...	ALAN B...	MANDEAL...	Justin.S...		15/06/20...	20/05/20...		
Alan.Finnie	Alan	Finnie	Drafting	Piping	Pipin...	Pipin...	Desig...	All	Perth	ALAN F...		Alan.K...		18/01/20...	20/05/20...		
Alan.Kern...	Alan	Kernag...	Drafting	Mechan...	Senior Ch...	Senior Ch...	Desig...	All	Perth	ALAN K...	ALAN KERN...	ashe...		04/11/20...	20/05/20...		
Alan.Page	Alan	Page	Drafting	Mechan...	Lead...	Lead Mec...	Desig...	All	Perth	ALAN P...	ALAN PAGE			30/09/20...	20/05/20...		
Alex.Barry	Alex	Barry	Engineer...	Process	Study Ma...	Study Ma...	Engin...	All	Perth	ALEX B...	ALEX BARRY	David.B...		08/06/20...	20/05/20...		
Alex.Liang	Alex	Liang	Engineer...	Control...	Contr...	Control S...	Engin...	All	Perth	ALEX L...		Chris.R...		16/11/20...	20/05/20...		
Alex.Reid	Alex	Reid	Administr...	Health...	Health C...	Health C...	Admi...	01785:02903:04964	Perth	FRANK...	FRANK MO...			13/11/20...	20/05/20...		
Alex.Tank	Alex	Tank	Developm...	Offsite...	Senior D...	Senior D...	Engin...	All	Perth	ALEX TA...	ALEX TANK			25/09/20...	20/05/20...		
Alexandra...	Alexandra	Hayes	Developm...	Offsite...	Senior D...	Senior D...	Admi...	All	Perth	ALEXA...		bride...		19/10/20...	20/05/20...		
alexandre...	Alexandre	Roy	Developm...	Offsite...	V-P D...	V-P Deve...	Engin...	All	Mont...	ALEXA...	CRAIG WES...	Jacque...		06/07/20...	20/05/20...		
Allan.Gar...	Allan	Garbutt	Drafting	General...	Drawin...	Drawin...	Admi...	All	Mont...	ALLAN...	ALLAN GAR...	Frederi...		23/04/20...	20/05/20...		
allison.pro...	Allison	Procter	Project M...	Offsite...	Project A...	Project A...	Admi...	All	Perth	ALLISO...		Paul.He...		01/07/20...	20/05/20...		
Anahita.M...	Anahita	Motearefi	Drafting	Electrical	E&I D...	E&I Desi...	Desig...	All	Perth	ANAHIT...		Chris.R...		16/12/20...	20/05/20...		

Change Log 18th May 2021

- Transactions to date is changed to All Transactions

-  Clients
-  Commodity Codes
-  Departments
-  Disciplines
-  Document Types
-  Exo Resources
-  Offices
-  Phases
-  Design Resource Planning
-  Roles
-  Tender Profiles
-  All Transactions
-  Unit of Measures
-  Users

- EXO -> Transactions
 - o Changed back end to server mode so that data is streamed from server
 - o Only issue is program will blink when updating records

Change Log 23rd April 2021

- Forecast
 - o Fixed a bug where EAC gets calculated incorrectly when P6 schedule data date is less than forecast data date

Grid Functions PF Functions Weeks Show Actuals History Save EAC Save Excel Summary Data Date 30/04/2021 End Date 30/11/2021 Save Dates P6 Schedule 20638-F/C ME 03.21 P6 Data Date 2/04/2021 Calculate Forecast																									
P6 Data date is less than Data date																									
n	Actual Costs (B)	Actual Cost Post DD	Outstanding (C)	Previous Total Commitment	Total Commitment (B + C)	Total Commitment Diff	Incommitter (D)	Prev. EAC (F)	EAC (E) (B + C + D)	Variance (A - E)	Period Move (G)	Percentage Period Move (G / F)	Oct-20	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21
0	2,107	\$4,520	\$0	\$0	\$4,520	\$4,520	\$0	\$151,922	\$153,993	\$156,442	-\$35,919	-\$2,450	-2%	\$0	\$259	\$0	\$0	\$0	\$4,261	\$0	\$142,186	\$0	\$0	\$0	\$0
EAC should be 142,186 (May-21 Forecast) + 4,520 (Actuals) = 146,706 but it is calculated as \$156,442 because EAC is calculated in the back end based on 3 components													Budget (A)	Oct-20	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21
													\$0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	144.29	2,107.08	0.00	0.00	0.00
													\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,736	\$142,186	\$0	\$0	\$0	
													\$0	\$0	\$0	\$0	\$0	\$0						\$0	
													\$0	\$0	\$259	\$0	\$0	\$0						\$0	
													\$0	\$0	\$0	\$0	\$0	\$0						\$0	
Actuals + P6 Forecast + Manually Override Costs																									
Grid Functions PF Functions Weeks Show Actuals History Save EAC Save Excel Summary Data Date 30/04/2021 End Date 30/11/2021 Save Dates P6 Schedule 20638-F/C ME 03.21 P6 Data Date 2/04/2021 Calculate Forecast																									
PF Units	Actual Costs (B)	Actual Cost Post DD	Outstanding (C)	Previous Total Commitment	Total Commitment (B + C)	Total Commitment Diff	Incommitter (D)	Prev. EAC (F)	EAC (E) (B + C + D)	Variance (A - E)	Period Move (G)	Percentage Period Move (G / F)	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	
2,107	\$4,520	\$0	\$0	\$4,520	\$4,520	\$0	\$142,186	\$153,993	\$146,706	-\$26,183	\$7,287	5%	\$259	\$0	\$0	\$0	\$4,261	\$0	\$142,186	\$0	\$0	\$0	\$0	\$0	
													Budget (A)	Nov-20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	
													\$0	0.00	0.00	0.00	0.00	0.00	0.00	2,107.08	0.00	0.00	0.00	0.00	
													\$0	\$0	\$0	\$0	\$0	\$0	\$142,186	\$0	\$0	\$0	\$0		
													\$0	New version accumulates P6 Forecast costs before the data date of 30/04/2021 to the first forecast month of May-21											
													\$0	\$259										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0										\$0	
													\$0	\$0							</				

Change Log 9th April 2021

- Design Cost/Charge Rate
 - o Added area and subarea category

Default Columns				
Area	Sub Area	Discipline	Department	Doc Type
* - Any Any Control Systems Engineering Any - Any Any Vendor Drafting Any - Any Any Piping Drafting Any - Any Any Process Engineering Any - Any Any Instrumentation and Control Engineering Any - Any Any Civil Drafting Any - Any Any Mechanical Engineering Any				

- Construct Cost Rate
 - o Added area, subarea and variation category

Drag a column header here to group by that column				
Area	Sub Area	Discipline	Commodity	Variation Code
* - Any Any Commissioning O03 Any - Any Any Electrical E04 Any - Any Any Electrical E02 Any - Any Any Electrical E30 Any - Any Any Electrical E80 Any - Any Any Piping P03 Any - Any Any Mechanical M99 VAR 029 CAT6A Cables - Any Any Electrical F10 Any				

Change Log 7th April 2021

- Changed all “Cost Group” column header description to “Discipline Code”
- Changed all “Cost Type” column header description to “Commodity Code”
- Old header description in sample view (Exo -> Transaction)

36302 Koolan Island Crusher Upgrade [36302] Design Progress [36302] Transactions						
Drag a column header here to group by that column						
Editable when authorised						
Sub Job	Cost Group	Cost Type	Stock Code	Variation Code	Description	
36302-000-00-D1	PR01	PFD	SF5		SCOTT FRECKELTON	
36302-000-00-D1	PR01	PFD	SF5		SCOTT FRECKELTON	
36302-000-00-D1	PR01	PFD	SF5		SCOTT FRECKELTON	
36302-000-00-D1	PR01	PFD	SF5		SCOTT FRECKELTON	
36302-000-00-D1	PR01	PFD	SF5		SCOTT FRECKELTON	
36302-000-00-D1	GE01	MTG	DL5		DAVID LANDWEHR	
36302-000-00-D1	GE01	MTG	DL5		DAVID LANDWEHR	
36302-000-00-D1	GE01	MTG	DL5		DAVID LANDWEHR	
36302-000-00-D1	GE01	MTG	DL5		DAVID LANDWEHR	
36302-000-00-D1	GE01	MTG	DL5		DAVID LANDWEHR	

-
-
- New header description in sample view (Exo -> Transaction)

[15660] Transactions						
Drag a column header here to group by that column						
Editable when authorised						
Sub Job	Discipline Code	Commodity Code	Stock Code	Variation Code	Description	
15660-000-00-I1	GP01	G30	AA9		ANTHONY ASTONE	
15660-000-00-I1	GP01	G30	AA9		ANTHONY ASTONE	
15660-000-00-I1	GP01	G30	AA9		ANTHONY ASTONE	
15660-000-00-I1	PM01	G22	BD5		BEN DRYDEN	
15660-000-00-I1	PM01	G05	DP12		DAVID PARATORE	
15660-000-00-I1	PM01	G05	DP12		DAVID PARATORE	
15660-000-00-I1	PM01	G05	DP12		DAVID PARATORE	
15660-000-00-I1	PM01	G05	DP12		DAVID PARATORE	
15660-000-00-I1	PM01	G05	ZR0		ZAC RADONICH	
15660-000-00-I1	PM01	G05	ZR0		ZAC RADONICH	

Change Log 31st Mar 2021

- Forecast

[00151] Forecast

Subjob ▲

Subjob column no longer showing because it's grouped

	Phase	Discipline	Room	Room Name	Variation	Budget (A)	Actual Units	Remaining Units	PF Units	Actual Costs (B)	Actual Cost Post DD
▶	Subjob: 00151					\$0	0	0	0	\$0	\$80
▶	Subjob: 00151-000-00-D1					\$12	0	0	0	\$0	-\$26
▶	Subjob: 00151-000-01-C1					\$400	0	0	0	\$0	\$0
▶	▶ Subjob: 00151-001-00-D1					\$7,980	13	0	0	\$551	\$0
▶	Subjob: 00151-002-00-D1					\$13,200	0	0	0	\$0	\$0
▶	Subjob: 00151-004-00-D1					\$3,840	18	0	0	\$1,788	\$93
▶	Subjob: 00151-005-00-D1					\$4,800	0	0	0	\$0	\$2,177
▶	Subjob: 00151-006-00-D1					\$0	0	0	0	\$0	\$1,927
▶	Subjob: 00151-007-00-D1					\$0	0	0	0	\$0	\$232
▶	Subjob: 00151-009-00-D1					\$0	0	0	0	\$0	\$7,776
▶	Subjob: 00151-010-00-D1					\$0	0	0	0	\$0	\$613

Previous Total Commitment	Total Commitment (B + C)	Total Commitment Diff	Incommitted (D)	Prev. EAC (F)	EAC (E) (B + C + D)	Variance (A - E)	Period Move (G)	Percentage Period Move (G / F)	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19
\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	1 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$12	\$0	3 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$400	\$0	2 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$551	\$551	\$0	\$0	\$552	\$551	\$7,429	\$0	8 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$13,200	\$0	2 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$1,788	\$1,788	\$0	\$0	\$1,788	\$2,052	-\$1,788	3 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$4,800	\$0	5 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	2 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	3 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$1	\$0	\$0	\$1	2 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	3 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0

Show total records and grouped records here since percentage period move doesn't have a summary

\$551	\$2,339	\$1,788	\$0	\$553	\$2,339	\$27,893	-\$1,786	34 Record(s)	\$0	\$0	\$0	\$0	\$0	\$0
-------	---------	---------	-----	-------	---------	----------	----------	--------------	-----	-----	-----	-----	-----	-----

- Scheduling Export

Grid

Scheduling

Check and Delete Assignments

Remap P6 Ids

Push to P6

Export Relationship

Export relationship assignment to excel

[20638] Design Budget

20638_001 - 20638-SCP-PM-63 -2 Mapping

Activity Id	Task	Type	Begin	End	Assigned Units	
A3170	Milestone 1 - sub...	Milestone	12-Mar-20	12-Mar-20	0	
A39270	Milestone 2 - sub...	Milestone	14-Apr-20	14-Apr-20	0	
A3180	Milestone 2 - sub...	Milestone	14-Apr-20	14-Apr-20	0	
A3190	Milestone 3 - sub...	Milestone	24-Aug-20	24-Aug-20	0	
A39280	Milestone 3 - sub...	Milestone	26-Aug-20	26-Aug-20	0	
A3260	Milestone 4 - sub...	Milestone	26-Oct-20	26-Oct-20	0	
A41460	SP4 - Raw and WW...	Milestone	09-Dec-20	09-Dec-20	0	
A41450	SP4 - Raw and WW...	Milestone	13-Jan-21	13-Jan-21	0	
20638-SCP-PM-63 -2	Koodaideri Mine N...	WBS			28,968	
1	PROJECT SCHEDULE	WBS			28,968	
1.2.6	Procurement	WBS			858	
1	SP1 - Entrance and...	WBS			32	
1	Architectural	WBS			32	
1	AR01 Modular Buil...	WBS			32	
1.3.17-ST03-...	ST01 Modular Buil...	Activity	20-Jan-20	10-Feb-20	32	
1.2.6.111	Emergency Respon...	WBS			0	
1.2.5-ST-...	ST01 EMO Modula...	Activity	15-May-20	10-Jul-20	0	
1.2.5-ST-...	ST01 EMO Modula...	Milestone	17-Aug-20	17-Aug-20	0	
1.2.5-ST-...	ST01 EMO Modula...	Activity	07-Sep-20	02-Nov-20	0	
1.2.5-ST-...	ST01 EMO Modula...	Activity	06-Oct-20	07-Apr-21	0	
1.2.5-ST-...	ST01 EMO Modula...	Activity	08-Apr-21	16-Apr-21	0	
1.2.6.112	Shower and Locker...	WBS			0	
1.2.4-ST-	ST01 Shower & Lo...	Milestone	20-Jul-20	20-Jul-20	0	

Activity Assignments

Activity:

Assignments

Deliverable

20638-REV-EL-211

Drag a column header here to group by that column

Change Log 17th Mar 2021

- S-Curve
 - Added department column, department column is a function of looking up doc types for default department, some doc types might be used across different department and thus might be inaccurate

Refresh

Save Layout

Reset Layout

Edit Report

View Report

Backward

Data Date

14-Mar-21

Forward

Disable Auto Report Date

Units

Costs

#2 Qty

% Percentage

#2 Absolute

All

Construct

Design

36302 Koolan Island Crusher Upgrade

Drag a column header here to group by that column

General									Cumulative					
Subjob	Phase	Area	Sub Area	Department	Discipline	Commodity	Total Planned Units	Total Current Units	Baseline Planned % to Date	Current Planned % to Date	Baseline Earned % to Date	Current Earned % to Date	Planned Units to Date	Current Units to Date
36302-000-00-11	I1	000	00	PM	PM01	G05	0.00	0.00	0.00%					0.00
36302-000-00-11	I1	000	00	AD	PM01	G07	0.00	0.00	0.00%					0.00
36302-000-00-11	I1	000	00	PM	PM01	G08	0.00	0.00	0.00%					0.00
36302-000-00-11	I1	000	00	PM	PM01	G22	0.00	0.00	0.00%					0.00
36302-000-00-11	I1	000	00	PM	PM01	G23	0.00	0.00	0.00%					0.00
36302-000-00-11	I1	000	00	PM	SM01	G01	0.00	0.00	0.00%					0.00
36302-000-00-11	I1	000	00	PM	SM01	G05	0.00	0.00	0.00%					0.00
Total 241 Records							13268.00	13268.00	76.35%	76.35%	56.85%	56.85%	10129.79	

- Excel export also shows lookup department

Type	Subjob_Name	Department_Co	Discipline_Name	Commodity_Co	Data_Date	Units	Costs	Actual_Costs
Burned	03608-115-00-D1	DRG	ME01	DRG	02/09/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	16/09/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	23/09/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	30/09/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	07/10/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	14/10/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	21/10/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	28/10/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	04/11/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	11/11/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	18/11/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	25/11/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	02/12/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	09/12/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	16/12/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	23/12/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	30/12/2018	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	06/01/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	13/01/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	20/01/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	27/01/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	03/02/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	10/02/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	17/02/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	24/02/2019	0	0	0
Burned	03608-115-00-D1	DRG	ME01	DRG	03/03/2019	0	0	0

Change Log 8th Feb 2021

- Design -> Variation
 - Added ability to auto reduce earned hours from latest date onwards to accommodate negative variation hours

⌵

📄 Export ✅ Check ❌ Uncheck

These deliverable have negative variation units that'll erode earn value when proceed, please select whether to:

1. Reduce earned by checking 'Reduce Earn Value'
2. Use max reducible units, overriding specified negative variation

A backup of progress will be automatically taken before variation approvals

Internal Name	Total Units	Earned Units	Maximum Reducible	Variation Reduction	Reduce Earn Value
X 00151-007-CAL-ST-002	100	50	-50	-75	☒

OK Cancel

In this instance, deliverable have 100 total hours and 50 hours already earned, but variation defines a 75 hours reduction, two options are available during approval

- Reduce earned hours ticked – Earned units will be reduced to 25 so that 75 hours reduction can be applied
- Reduce earned hours not ticked – Variation hours will be changed to 50 hours reduction instead of 75, as defined by maximum reducible units column

Cont. Change Log 8th Feb 2021

- Added ability to reduce earned units when variations are unapproved

These deliverable have negative variation units that'll erode earn value when proceed, please select whether to:

1. Reduce earned by checking 'Reduce Earn Value'
2. Use max reducible units, overriding specified negative variation

A backup of progress will be automatically taken before variation approvals

Internal Name	Total Units	Earned Units	Maximum Reducible	Variation Reduction	Reduce Earn Value
00151-007-CAL-ST-002	100	50	-50	-100	☐

OK Cancel

For instance, a variation that was previously approved with 100 hours is now in the process of unapproval. Since 50 hours has already been earned, 2 options are available during unapproval

- Reduce earned hours ticked – Earned units will be reduced to 0 so that unapproval with 100 hours taken away from the deliverable can take place
- Reduce earned hours unticked – Earned units will not be reduced, but user will see negative 100 hours remaining in progress

Change Log 27th Jan 2021

- Forecast

- Added ability to save forecast data to be retrieved by excel

Drag a column header here to group by that column

Phase	Subjob	Disciplr	mmoc	ommodi Name	Variation	Budget (A)	ctual Uni	remainin Units	PF Units	Actual Costs (B)	ctual Cos Post DD	Outstanding (C)	Uncommitted (D)	Prev. EAC	EAC (E) (B + C + D)	Variance (A - E)	Period Move	Feb-21
D1	00151-001-00-D1	GE01	MAN	MAN -...		\$0	0	0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
D1	00151-001-00-D1	EL02	DRG	DRG -...	VA001	\$1,800	0	0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,800	\$0	\$0
D1	00151-001-00-D1	EL02	DRG	DRG -...	VA002	\$1,300	0	0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,300	\$0	\$0
D1	00151-001-00-D1	GE02	MAN	MAN -...		\$1,000	0	0	0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,000	\$0	\$0
D1	00151-001-00-D1	ST01	CAL	CAL -...		\$400	13	0	0	\$551	\$0	\$0	\$0	\$0	\$551	-\$151	-\$551	\$0

Change Log 25th Jan 2021

- Project S-Curve
 - o Added ability to move data date forward/backward
 - o Added ability to disable report date auto change to previous period ending



- Progress
 - o Added ability to disable report date auto change to previous period ending

[03608] Progress							
Drag a column header here to group by that column							
	Name	Type	Start Date	Data Date	Previous Report Date	Report Date	Disable Auto Report Date
*	03608DAILY_001	Construct	2018-09-16	2020-11-12		2021-01-07	☐
I	03608WEEKLY_001	Design	2018-09-16	2020-11-08		2021-01-03	☒

Change Log 13th Jan 2021

- Register -> Change Register
 - o Added design change notice

30202] Change Register														
Drag a column header here to group by that column														
Change Number	Area	Title	Issue Description	TQ Number	Schedule Impact	Cost Impact	EPCM Hrs Impact	Avg Hr Rate (\$/h)	EPCM Cost Impact (\$)	CAPEX Impact (\$)	Total Cost Impact (\$)	Comments	Raised By	Date R
Click here to add a new row														
001	400	Addition of Hydrogen Product Flow Meter	Project originally intended to meter hydrogen production by calculation of flow to tube trailers. Tube trailers no longer in scope. Produced hydrogen is used for fuel cell and balance sent to flare. Produced hydrogen would need to be determined by calculation based on fuel cell consumption, pressure drop across PCV to flare, and PCV position. This would not be accurate. Hazer have confirmed that they would like a flow meter to be added to this like. Est. budget price \$6k (supply) for a Vortex flow meter. Additional datasheet for new flow meter.		Potential	Yes			\$0		\$0			22/10/

DESIGN CHANGE NOTICE				
DOCUMENT NUMBER	30202-CN-001		REVISION	A
DATE SUBMITTED	22-Oct-20			
PROJECT TITLE	30202 - Hazer Commercial Demonstration Plant			
ORIGINATOR - CHANGE INFORMATION				
CHANGE TITLE	Addition of Hydrogen Product Flow Meter			
WBS AREA	400			
IMPACT	☒ Client		☐ Internal	
PRIORITY	☐ Low	☐ Medium	☐ High	☐ Mandatory
CHANGE DESCRIPTION				
Project originally intended to meter hydrogen production by calculation of flow to tube trailers. Tube trailers no longer in scope. Produced hydrogen is used for fuel cell and balance sent to flare. Produced hydrogen would need to be determined by calculation based on fuel cell consumption, pressure drop across PCV to flare, and PCV position. This would not be accurate. Hazer have confirmed that they would like a flow meter to be added to this like. Est. budget price \$6k (supply) for a Vortex flow meter. Additional datasheet for new flow meter:				
EPCM HOURS IMPACT				
EPCM COST IMPACT	\$0			
CAPEX IMPACT				
TOTAL COST IMPACT	\$0			
SCHEDULE IMPACT	Potential			
ORIGINATOR	Name		Signature	
APPROVER	Name		Signature	
CLIENT - APPROVAL				
DECISION	☐ Approved		☐ Approved as noted	
	☐ Not approved		☐ More info required	

Change Log 8th Jan 2021

- Design -> Progress
 - o Added user remaining units to add discretionary remaining units

[00151] Design Progress														
leader here to group by that column														
					Editable Properties				Budget (Read Only)					
Client Number	Primary Title	Secondary Title	Comments	Sub Job	Gates	Current %	Target Start	Target End	Budget Hours	Adjusted Budget	Variation Hours	Approved Variations	Total Hours	User Remaining Hrs
Click here to add a new row														
	Iron Bridg...			00151-009-00-D1		0%			0.00	0 hrs	60.00	Expand t...	60.00	0.00
	Tianqi Pip...			00151-004-00-D1		0%			0.00	16 hrs	0.00	Expand t...	16.00	0.00
	Degrussa...			00151-010-00-D1		0%			0.00	0 hrs	23.00	Expand t...	23.00	0.00
001	Horsco Ba...			00151-001-00-D1		0%			0.00	20 hrs	0.00	Expand t...	20.00	10.00
001	Albemarle...			00151-006-00-D1		0%			0.00	30 hrs	0.00	Expand t...	30.00	0.00
2	Design Ma...			00151-000-00-D1		100%			0.00	0 hrs	0.00	Expand t...	0.00	0.00
1				00151-001-00-D1		0%			0.00	4 hrs	0.00	Expand t...	4.00	0.00
	Soda Ash...			00151-005-00-D1		0%			0.00	20 hrs	0.00	Expand t...	20.00	0.00

- Forecast
 - o Show user remaining units in forecast. Must be activated by column chooser (Right clicking on header and choose "Show Column Chooser")

The screenshot displays a software interface with a context menu open over a table. The menu options are: Sort Ascending, Sort Descending, Clear Sorting, Group By This Column, Hide Group Panel, Show Column Chooser (highlighted with a red box), Best Fit (all columns), Filter Editor..., and Show Search Panel. Below the menu, a table is visible with columns: Phase, Subjob, isciplir, nmoc, ommodir Name, Variation, Budget (A), ctual Uni, lemmainin Units, and p. A 'Column Chooser' dialog box is also open, showing a search bar and a list of columns with checkboxes. The 'User Remaining Units' checkbox is highlighted with a red box.

Phase	Subjob	isciplir	nmoc	ommodir Name	Variation	Budget (A)	ctual Uni	lemmainin Units	p
D1	00151-001-00-D1	GE01	MAN	MAN -...		\$0	0	4	
D1	00151-001-00-D1	EL02	DRG	DRG -...	VA001	\$1,800	0	0	
D1	00151-001-00-D1	EL02	DRG	DRG -...	VA002	\$1,300	0	0	
D1	00151-001-00-D1	GE02	MAN	MAN -...		\$1,000	0	0	
D1	00151-001-00-D1	ST01	CAL	CAL -...		\$400	13	20	
D1	00151-001-00-D1	ST01	CAL	CAL -...	VO001	\$480	0	0	
D1	00151-001-00-D1	GE01	MAN	MAN -...	21-36 H...	\$600	0	0	
D1	00151-001-00-D1	ST01	CAL	CAL -...	21-36 H...	\$2,400	0	0	
C1	00151-000-01-C1	EL02	E30	E30 S...		\$400	0	0	
C1	00151-000-01-C1	GP01	G99	G99 P...		\$0	0	10	
D1	00151-002-00-D1	ST01	CAL	CAL -...	002 - Sal...	\$12,000	0	0	
D1	00151-002-00-D1	GE01	MAN	MAN -...	002 - Sal...	\$1,200	0	0	
D1	00151-004-00-D1	ST01	CAL	CAL -...		\$1,920	0	16	
D1	00151-004-00-D1	ST01	CAL	CAL -...	004 - Tia...	\$1,920	0	0	
34 Rec...						\$30,232	13	183	183

Change Log 12th Nov 2020

- Design -> Deliverables Gates
 - o Deliverable gates goes by phases to support differentiation between D1, D2

Change Log 5th Oct 2020

- Design -> Progress
 - o Certain users will always open progress screen with previous week's data date. These users can also change progress data date, and it will not interfere with the data date for user that does not have the permission uses. The permission is as follows

Search		
Permission	Assigned	Read Only
▾ Dashboards		
My Dashboard	☐	
My Deliverables	☒	
▾ My Design Timesheet	☒	
Unsubmit EXO timesheet	☒	
Review Timesheets	☒	
Document Control	☐	
▾ Projects	☒	
HSE Report	☒	
▾ XXXXX	☒	
▾ Design		
▾ Deliverables	☒	
Approve deliverable's internal and client numbers	☒	
Unapprove deliverable's internal and client numbers	☒	
Book time for other users	☒	
Finalise deliverable's internal and client numbers	☒	
▾ Progress	☒	
Update deliverable's progress by qate/status	☒	
Always use previous week's date for progress and can change progress screen date	☐	
Progress Distribution	☒	
Variations	☒	
Deliverable Gates	☒	
Job Permissions	☒	
Variations	☐	
▾ Construct		
Job Setup	☒	
Resource Allocation	☒	
Cost Rates [Direct]	☒	
▾ EXO		
▾ Transactions	☒	☐
Show costs on EXO transactions	☒	
Allow changing quantity in EXO transaction	☐	
▾ Timesheets	☒	
Allow commit to EXO	☒	
Timesheets Query	☒	
▾ Jobs	☒	
Change budget in EXO	☒	
Master Job Permissions	☒	
Purchase Orders	☒	☐
Job History	☒	

Change Log 30th September 2020

- Exo -> Jobs
 - Not showing cost group and cost type error when stock code is VA001
 - Only validate cost group and cost type for new item in master job
 - Show duplicate error when committing to EXO
- Design -> Variations
 - Variation codes are pushes with default stock code item without cost group and cost type so that it doesn't clutter up forecast view

Change Log 11th September 2020

- Construction -> Variation
 - Allow negative values for revenue
- Construction -> Variation -> Variation Items
 - Remove cost group and cost type
 - Filter sub job in construction variation to show valid sub job codes only
 - Show cell error when sub job codes isn't valid for chosen type

Change Log 10th September 2020

- Forecast -> Forecast
 - Show empty cost group and cost type in forecast to accomodate variations without cost group and cost type coming from construction variation module

Change Log 9th September 2020

- Exo -> Jobs
 - Fixed an issue where committing to EXO resulting in empty cost group and cost type
- Design -> Risk Register
 - Revised risk register matrix

Change Log 7th September 2020

- Design -> Progress
 - Fixed an issue where at completion units doesn't match budgeted units when pushing to P6
 - Add a checkbox to allow certain projects to have current week ending data date
 - Added a button to copy start date to target start date and due date to target end date

Change Log 4th September 2020

- Design -> Progress
 - Data date will automatically change to current week data date when current day is the day of week for current week's data date

Change Log 1st September 2020

- Exo -> Jobs
 - Not validating/show errors on cost group and cost type when variation stock code is used
- Construction -> Variation
 - Group jobs by Sub Job code and commit to Exo using default stock code
- Forecast -> Forecast
 - Use total unapproved variation revenue to show unapproved revenue in forecast view

Change Log 24th August 2020

- Construction -> Variation
 - Added construction variation module
[Tutorial](#)

Change Log 29th July 2020

- Forecast -> Forecast

- Added column to show actual labour units post data date

Change Log 22nd July 2020

- Forecast -> Forecast
 - Removed colors from actuals history

Change Log 21st July 2020

- Exo -> Transaction, Exo -> Purchase Orders
 - Added stock code

Change Log 17th July 2020

- Design -> Deliverables / Progress
 - Added show variation name and approve units column

[How to check variation name and approved units](#)

Change Log 15th July 2020

- Design -> Deliverables
 - Added hidden column to allow subcontract hours to be excluded from forecast
- [How to exclude subcontract hours from forecast](#)

Change Log 14th July 2020

- Forecast -> Forecast
 - Added permission to allow user to edit construction forecast as uncommitted

Change Log 7th July 2020

- Design -> Job Permission
 - Fixed an error where newly added user isn't shown after refresh
 - Show only active users

Change Log 3rd July 2020

- Design -> Deliverables
 - Fixed an issue where subjob variation code doesn't show up in book time

Change Log 2nd July 2020

- Forecast -> Forecast
 - Try to fix an issue where module loads partial data
 - Not highlighting cells in green/red when date column's value is caused by PF changes
 - Try to fix summary calculation double up
 - Highlight PF column in green/red
 - Allow construction jobs cells to be edited when P6 project doesn't exists

Change Log 1st July 2020

- Allow user with permission to edit Exo -> Transaction quantity
- Editing Exo -> Transaction quantity will adjust line cost, line charge, line total, line total tax, line tax and linetotal incl tax in EXO
- Exo -> Timesheet narrative will be saved on day with hours so that when it's approved the narrative will be transferred over

Change Log 26th June 2020

- Design -> Deliverables
 - o Highlight duplicate client number in red
 - o Book Time dialog loads faster for user that doesn't have authority to book time for other users

Change Log 25th June 2020

- Forecast
 - o Uncommitted values can only be entered on procurement jobs
 - o Pasting uncommitted values on non-procurement jobs will show no results

[Test Case Clip](#)
